

**Project Name**

**Design** 5 activities

		151	03/25/19A	01/31/20A
--	--	-----	-----------	-----------

**Preconstruction**

50	KY Permit Review Period	45	01/30/20A	04/03/20A
60	BP-A Bid Period	13	02/07/20A	02/26/20A
70	Bid Review / Recommendation to Award	5	02/26/20A	03/04/20A
75	Scope Review Meetings	7	02/26/20A	03/06/20A
77	Award Subcontracts	15	03/04/20A	03/25/20A

**Construction**

**Site Work**

80	Mobilize	0	04/27/20	
90	Underground Utilities	20	04/27/20	05/22/20
100	Site Fencing & Mass Excavation	20	05/04/20	06/01/20
263	Fine Grade & Site Concrete Walks/Curbs	25	04/02/21	05/06/21
264	Landscaping & Irrigation	20	05/07/21	06/04/21
266	Demo/Replace Existing Asphalt	10	06/07/21	06/18/21
268	Site Caulking & Furnishings	10	06/21/21	07/02/21

**Foundations**


110	Drilled Piers	10	05/26/20	06/08/20
105	Concrete Foundations	35	06/02/20	07/21/20
120	Under Slab Utilities	20	06/30/20	07/28/20
130	Slab on Grade Prep & Pour	10	07/29/20	08/11/20
140	CMU Stair & Elevator Shafts	30	08/05/20	09/16/20

**Structure**

150	Steel Framing Install & Pour Level 1	20	08/26/20	09/23/20
160	Steel Framing Install & Pour Level 2	20	09/14/20	10/09/20
170	Steel Framing Install & Pour Level 3	20	09/30/20	10/28/20
180	Steel Framing Install & Pour Level 4	20	10/19/20	11/16/20
190	Steel Framing Install & Pour Level 5	20	11/02/20	12/01/20
200	Steel Framing Install & Detail Roof	15	11/17/20	12/08/20

**Building Envelope**

185	Detailing for Fiber Cement/Metal Panel	20	11/17/20	12/15/20
240	Masonry East Elevation	10	11/24/20	12/08/20

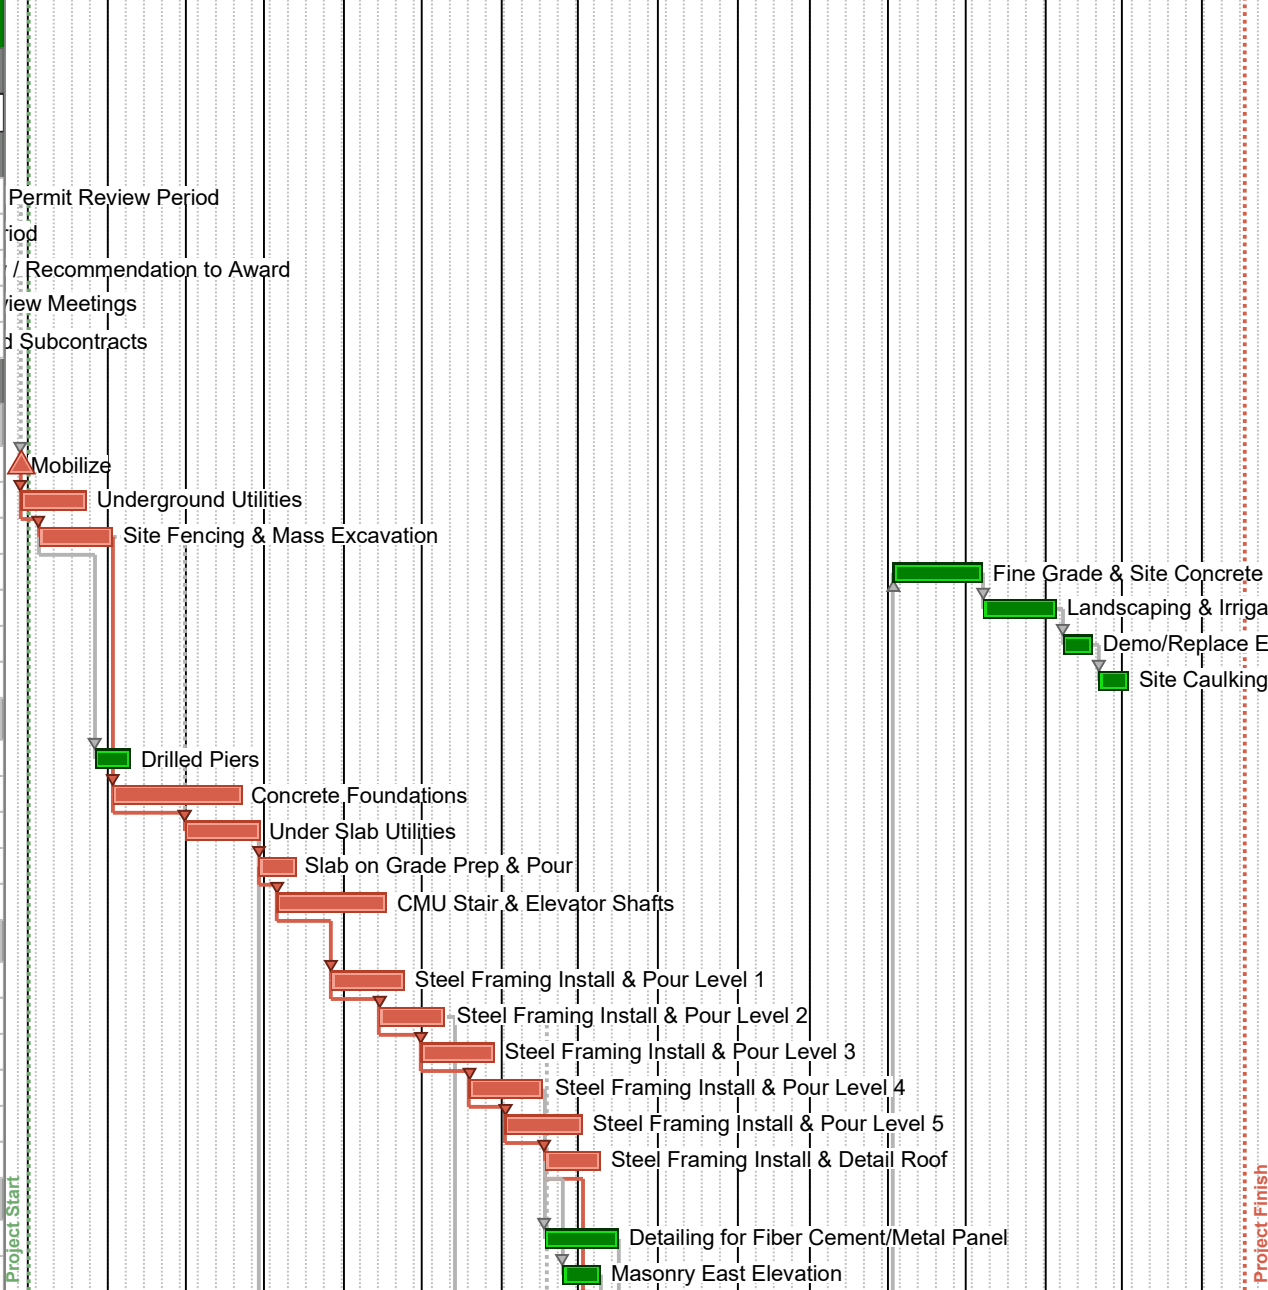

Start Date: 05/01/20  
 Finish Date: 08/16/21

Northern Kentucky University  
 New Residence Hall  
 Preliminary Construction Bid Schedule  
 1/30/2020



